

### Stakeholders:


- ANSPs

**FOC:** 12/2021

**Estimated achievement:** 12/2021


**On time**

**Average progress among States that have not yet completed the objective**



<b>SESAR Solutions:</b>	Solution #27
<b>SESAR Key Features:</b>	Advanced Air Traffic Services
<b>PCP Sub-Functionality:</b>	Pre-requisite for S-AF 3.2 Free Route (PCP)
<b>ICAO ASBU:</b>	B1-FRTO
<b>OI Steps:</b>	CM-0202, CM-0203, CM-0205, CM-0207-A
<b>Network Strategy Plan:</b>	SO3/1, SO4/1

### Completion Rate Evolution (% of States completed the objective)

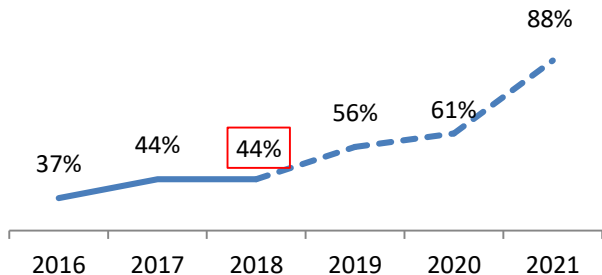


### Main 2018 developments:


MTCD in 2018 was declared completed by 18 States, showing no progress compared to 2017. The number of ANSPs progressing on time (i.e. Ongoing) decreased to 17 in 2018, from 20 in 2017. Implementation of MTCD is completed in 30 ACCs (27 in 2017), representing 43% of the applicable area. Tactical Controller Tool, an optional feature, has been completed so far in 8 ACCs (as in 2017). Work is progressing in 7 ACCs, and plans exist for another 14. Conformance monitoring function is the most deployed feature, completed in 36 ACCs (23 in 2017). Resolution support function is implemented in 18 ACCs. This latter feature was monitored for the first time in 2018. Overall the objective is progressing at a relatively fast pace and the completion criteria (80% completion rate) is expected to be reached within the FOC date. Full completion is nonetheless expected not before 2022, one year later than the FOC date of the objective.

### ATC12.1 - Automated Support for Conflict Detection, Resolution Support Information and Conformance Monitoring

Legend	
Completed	18
Ongoing	17
Planned	1
Late	4
Not yet planned	1
Not Applicable	0
Missing Data	0
Undefined	0



**Applicability Area:**  
All ECAC States except LU

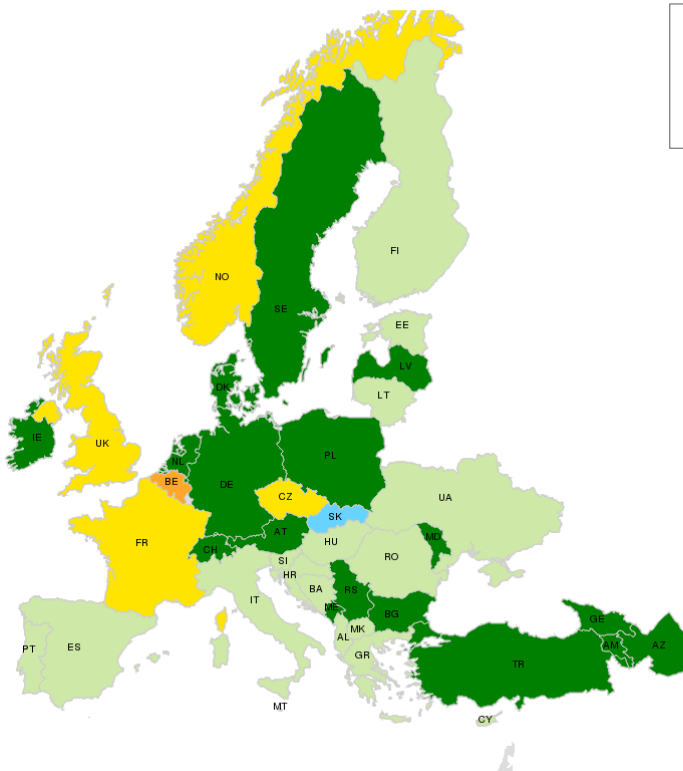

Overlaps		
Code	Full name	Progress
MAS	Maastricht UAC	Completed
MT	Malta	Ongoing
