



# ITY-AGVCS2 Implement AGVCS below FL195

### Stakeholders:

- ANSPs
- Airspace Users
- Military
- Network Manager
- Regulators
- Airport Operators

**Radio equipment:** 12/2017


**Freq. converted:** 12/2018

**State Aircraft:** 12/2020

**Est. achievement:** 12/2023

**Late**

### Average progress among States that have not yet completed the objective



**SESAR Solutions:** -

**SESAR Key Features:** Enabling Aviation Infrastructure


**EOC/OC:** -

**ICAO ASBU:** No corresponding ASBU

**OI Steps:** CTE-C01a

**Network Strategy Plan:** SO8/1

### Completion Rate Evolution (% of States completed the objective)


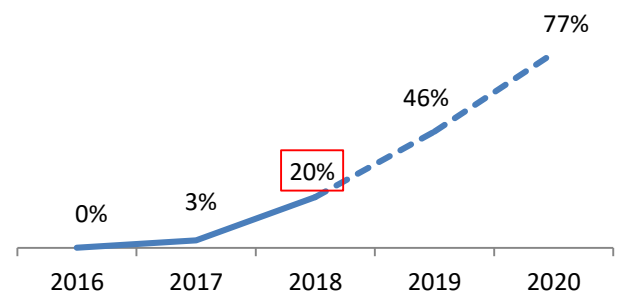


### Main 2018 developments:

As the date for the conversion of frequency assignments to 8.33 kHz has passed, the objective is to be considered as "Late". Only 7 States have reported completion while 15 States have reported delays in the implementation of the objective. During the reporting cycle, 70% of the conversions initially planned for 2018 have been achieved amounting to 1995 converted assignments. The delay is mostly caused by the deferred conversion of aerodrome assignments or of those used by the military stakeholders and are due to the high number of non-equipped aircraft, in particular General Aviation and State aircraft. Fortunately these assignments have a limited impact on the Network. The EC has tasked EUROCONTROL NM, through the 8.33 VCS ISG, to take a central role in the coordination of the implementation of 8.33kHz below FL195 and it is still strongly recommended that all States and in particular ECAA, actively participate in the group.

ITY-AGVCS2 - 8,33 kHz Air-Ground Voice Channel Spacing below FL195

| Legend          |    |
|-----------------|----|
| Completed       | 7  |
| Ongoing         | 12 |
| Planned         | 0  |
| Late            | 15 |
| Not yet planned | 0  |
| Not Applicable  | 1  |
| Missing Data    | 0  |
| Undefined       | 0  |

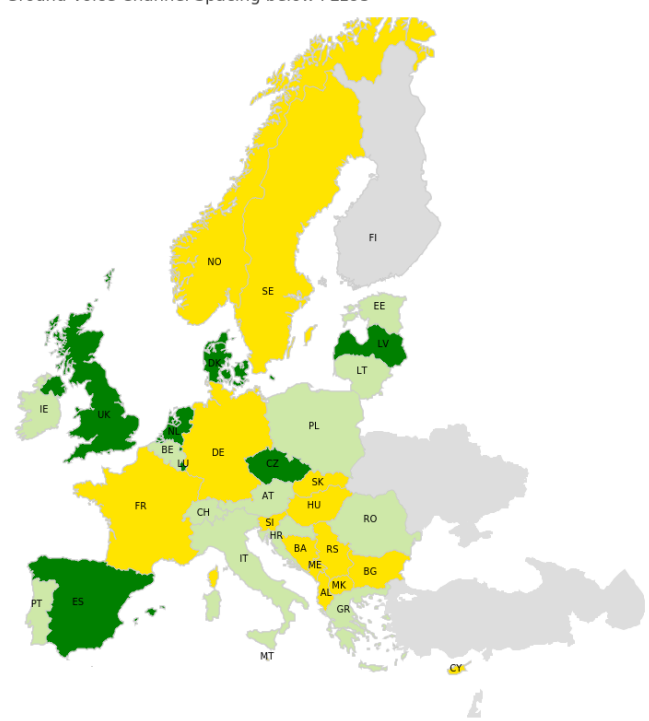

**Applicability Area:**  
All EU+ States except GE and MD

| Overlaps |            |           |
|----------|------------|-----------|
| Code     | Full name  | Progress  |
| LU       | Luxembourg | Completed |
| MT       | Malta      | Late      |
